

**BINGO Eastern Creek Landfill
Update on Permanent Flare works:
Drilling program and leachate riser upgrade**

August 2022 – Weekly Update: w/c 29 August

Executive Summary

Work on the landfill gas collection system (LFGCS) at our Eastern Creek site remain on schedule.


Highlights from Week 4 (w/c 29 August) include:

- Flares 7 and 8 have been installed (8 flares are now online).
- New wells (A059 – A064) are now online and connected to the 355mm gas line.
- Stage 3 drilling to be completed 1 September 2022, marking the end of the deep drilling for the project.
- Stage 4 and 5 of 355mm main gas line installed and wells connected in that area.


Week 5 (w/c 5 September) will be focused on the following activities:

- Commencing works for the centre main gas line 355mm.
- Preparing flow lines from recent drilled wells.
- Commencing fabrication for new flares (offsite).
- Welding gas pipe for stages 6 to 10 of 355mm main gas lines.
- Welding gas pipe for 450mm header lines

Live as Built – Grey completed, Colour still to complete

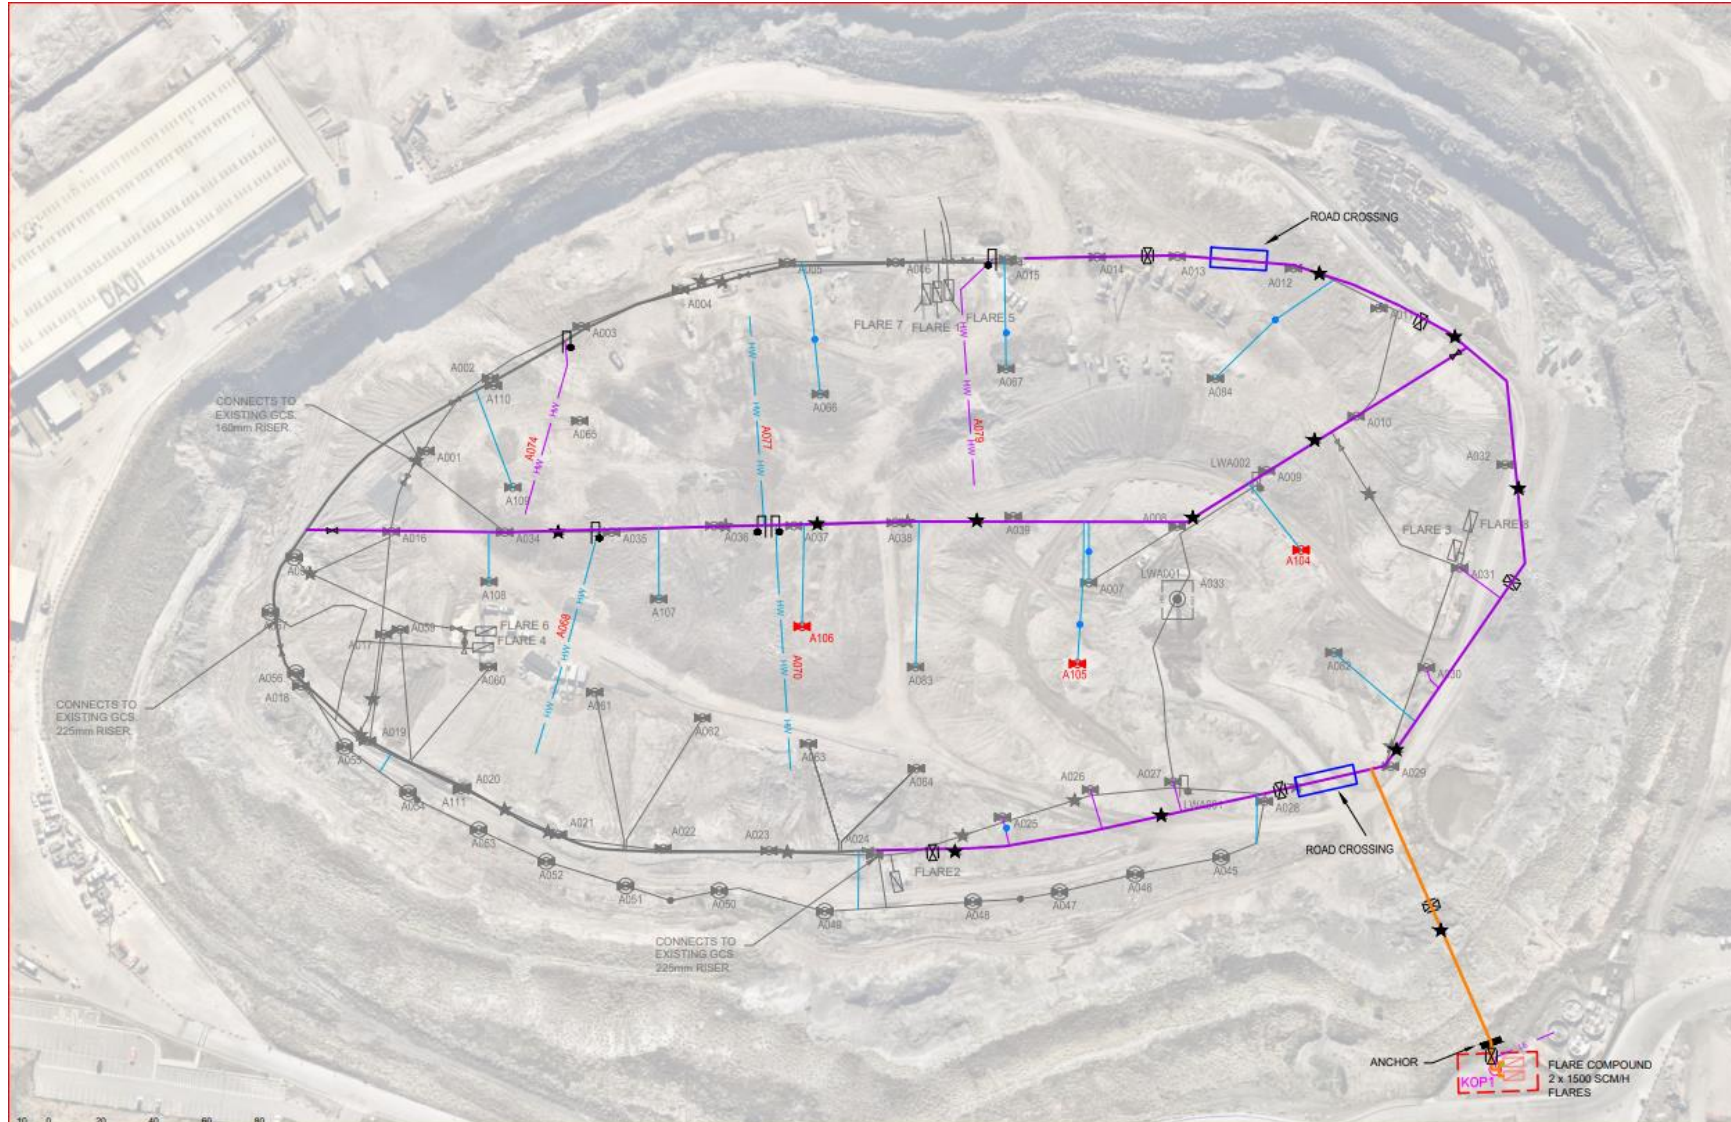

Week 4: Program Works – LFG 355mm Line

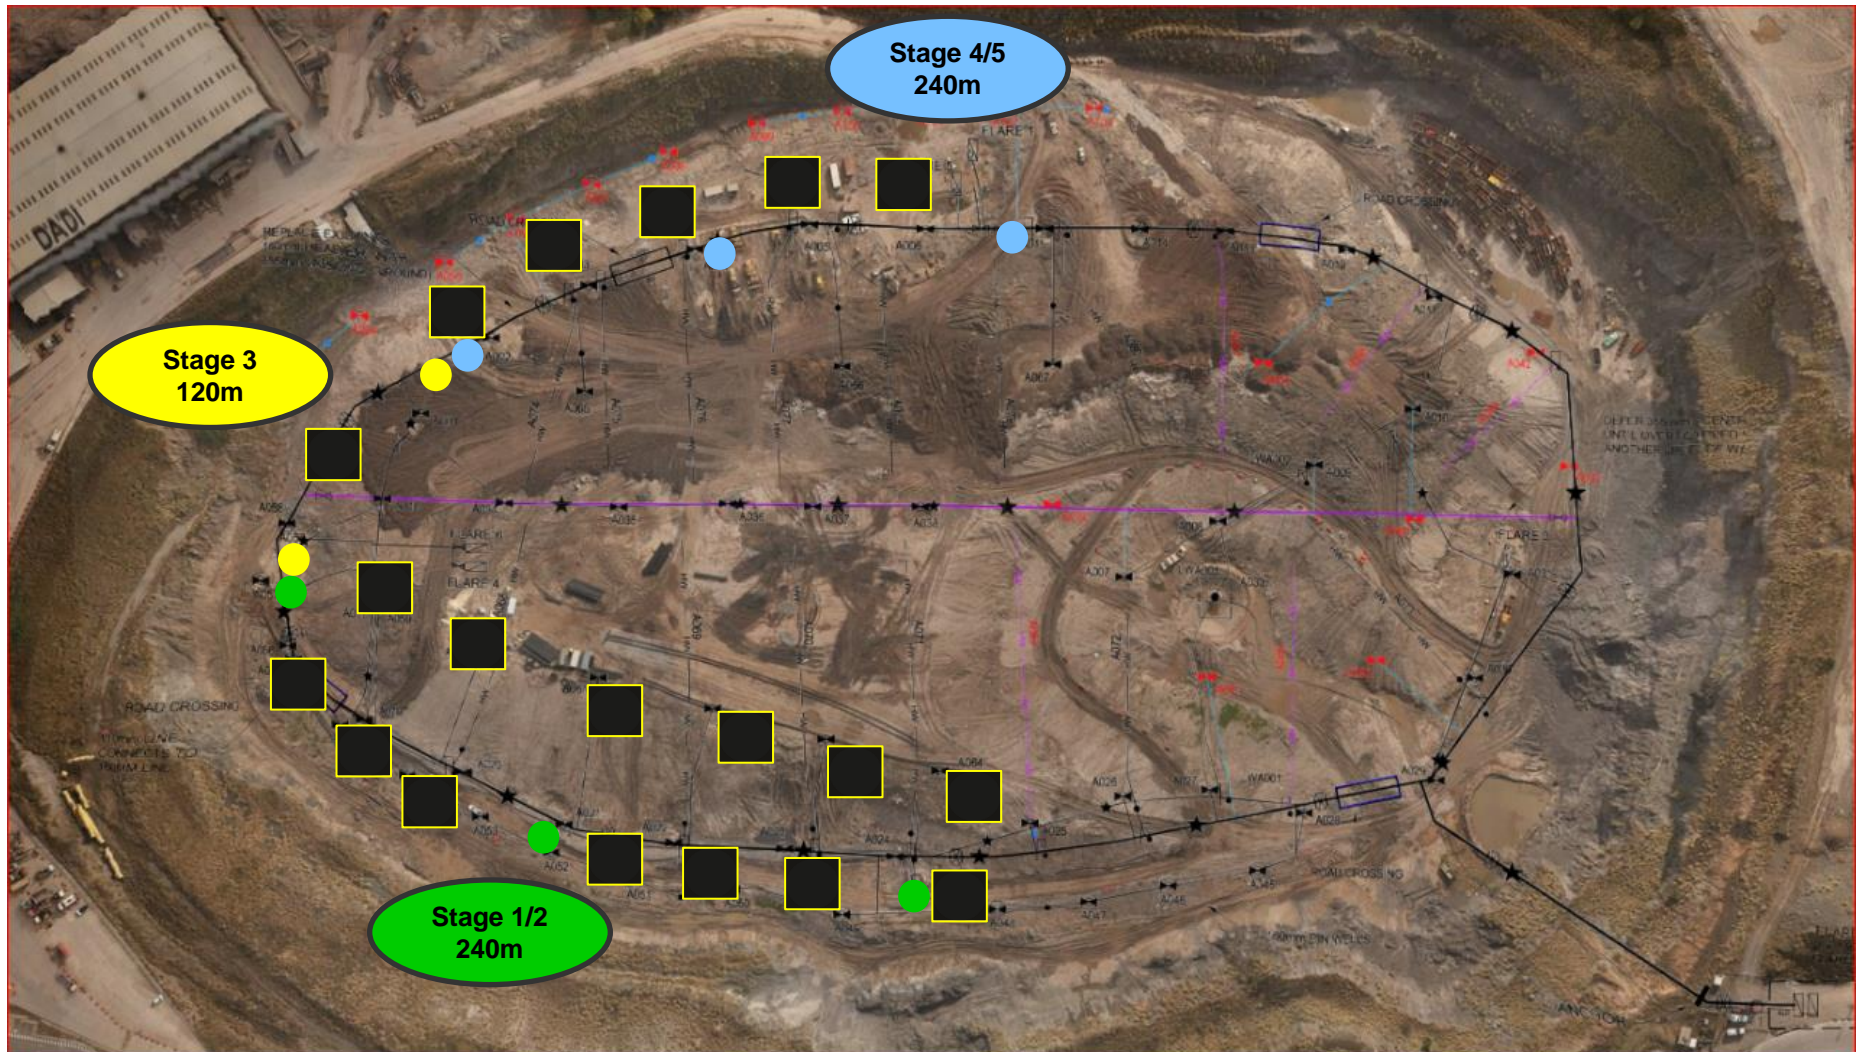

 19 wells now active on the new 355mm gas line

Flare Overview – as at 29 August 2022

Flare 1	Flare 2	Flare 3	Flare 4	Flare 5	Flare 6	Flare 7	Flare 8
Bio-Gas 500m ³ per Hour	Bio-Gas 700m ³ per Hour	Run Energy 500m ³ per Hour	Run Energy 500m ³ per Hour	Run Energy 500m ³ per Hour	Run Energy 500m ³ per Hour	LGI Energy 500m ³ per Hour	LMS Energy 300m ³ per Hour
Running	Running	Running	Running	Running	Running	Running	Running
North	South	East	West	North	West	North	East
						Now Online	Now Online

Flare Overview – 8 flares now running

